ID	Task Name	Duration	Start	Finish
1	**CORDOVA PSE DESIGN**	**614 days**	**Thu 6/29/23**	**Wed 11/5/25**
2	30% PSE	21 days	Thu 6/29/23	Thu 7/27/23
3	TxDOT 30% Review	21 days	Fri 7/28/23	Fri 8/25/23
4	60% PSE	44 days	Mon 8/28/23	Thu 10/26/23
5	TxDOT Review	21 days	Fri 10/27/23	Fri 11/24/23
6	90% PSE	79 days	Mon 11/27/23	Thu 3/14/24
7	ROW and Utilities	15 mons	Fri 3/15/24	Thu 5/8/25
8	Final plans	2 mons	Fri 5/9/25	Thu 7/3/25
9	Letting	0 days	Wed 11/5/25	Wed 11/5/25
10				
11	**ROW Acquisition**	**244 days**	**Mon 8/7/23**	**Thu 7/11/24**
12	Survey	25 days	Mon 8/7/23	Fri 9/8/23
13	Legal descriptions/ROW maps	17 wks	Mon 8/14/23	Fri 12/8/23
14	Title commitments and research	4 wks	Mon 12/11/23	Fri 1/5/24
15	Appraisal inspection and report	8 wks	Mon 1/8/24	Fri 3/1/24
16	Initial offers	30 days	Fri 3/8/24	Thu 4/18/24
17	Final offers	60 days	Fri 4/19/24	Thu 7/11/24
18				
19	**Environmental**	**120 days**	**Fri 9/22/23**	**Thu 3/7/24**
20	PCR	4 wks	Fri 9/22/23	Thu 10/19/23
21	Public Meeting	0 days	Thu 11/2/23	Thu 11/2/23
22	* CE	6 mons	Fri 9/22/23	Thu 3/7/24
23				
24	**Utilities**	**529 days**	**Fri 10/27/23**	**Wed 11/5/25**
25	Design	6 mons	Fri 10/27/23	Thu 4/11/24
26	*Materials	6 mons	Fri 4/12/24	Thu 9/26/24
27	Relocation (Max Allowance)	289 days	Fri 9/27/24	Wed 11/5/25
28	Relocation (PSE Schedule)	160 days	Fri 9/27/24	Thu 5/8/25

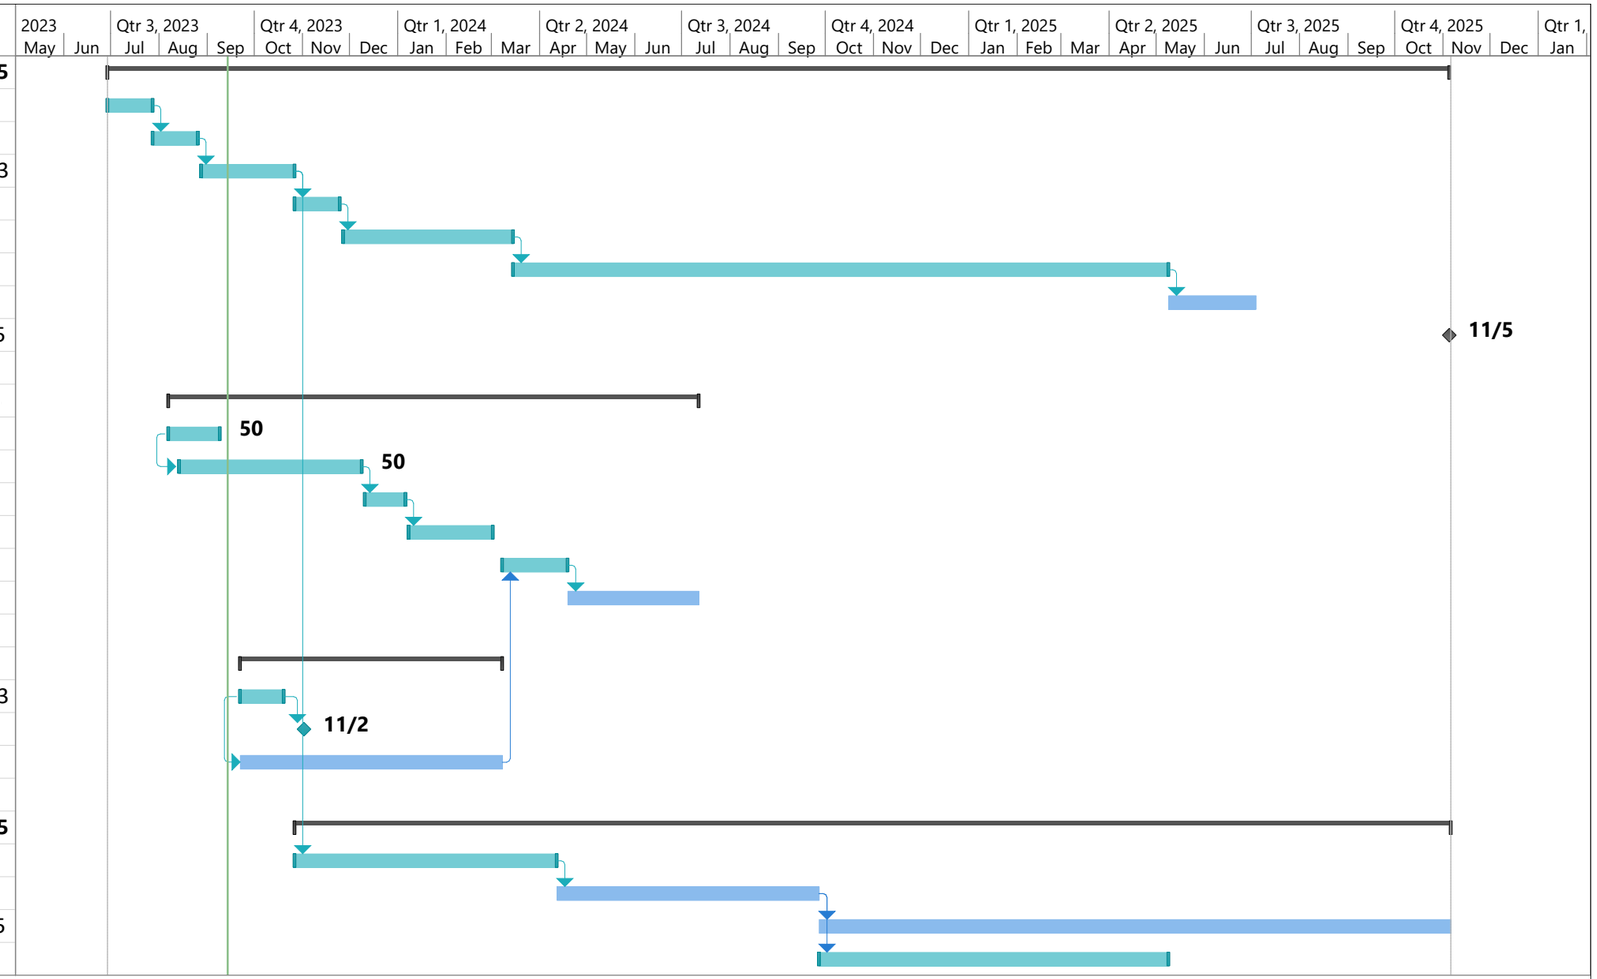

*Subject to change

Project: Cordova Rd Schedule
Date: Thu 9/14/23

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			
